


WSDOT Project Delivery Method Review

SR 526 Corridor Improvements

Gregory Cook, P.E., Project Engineer July 24th, 2024

Project Location

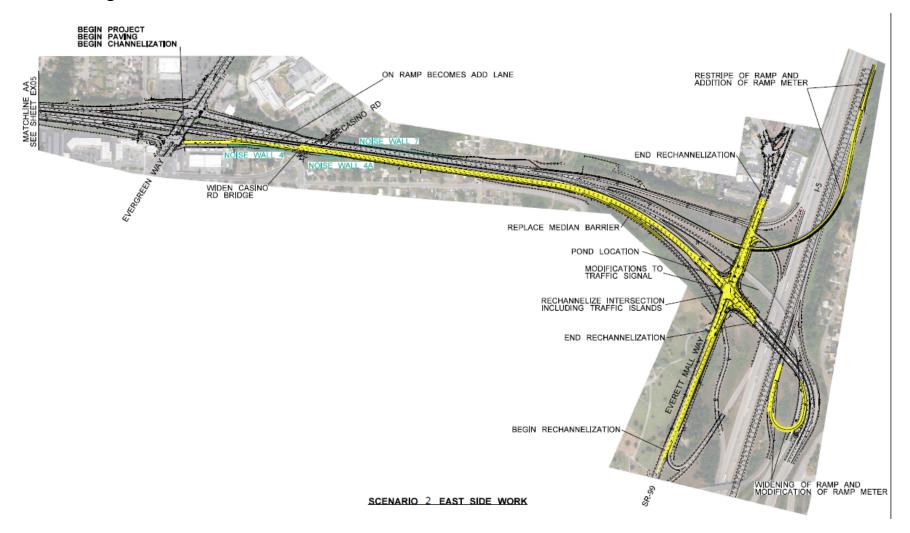

Scope of Work

- Improvements will start from Evergreen Way to I-5:
 - Convert an existing HOV lane to create a third general-purpose lane between Evergreen Way and I-5
 - Widen the bridge over Casino Rd
 - Widen the roadway in the eastbound direction
 - Rechannelize the intersection with Everett Mall Way
 - Install ramp meters from EB SR 526 to NB I-5
 - Construct noise walls

Other improvements

- Repaving HMA
- Removal and replacement of median and shoulder barriers
- Signal modification, illumination and ITS
- Landscaping, drainage, runoff treatment and detention

* % Design Complete

- 90% design was completed in December 2023
- 100% PS&E will be submitted August 2024

Schedule

- AD Prior to Legislative Request for CPARB Review: September 16, 2025
- Revised AD to Account for CPARB Review: January 6, 2025
- Begin Construction April 2025
- Physical completion June 2027

Project Delivery

Design-bid-build

Funding Source and Requirements

- Connecting Washington funding
- Bid price will need not exceed allocated funding

	Authorized Budget	Cost to Date	
PE	\$11.1M	\$10.2M	
ROW	\$0M		
Construction	\$35.4M - \$36.1M		
Total	\$46.5M - \$47.2M -		

Environmental Documentation Status

	Document Title	Complete Date	Anticipated Complete Date
1	NPDES Stormwater Construction General Permit		11/1/24
2	Section 106 Exemption for Culture	3/28/24	
3	Programmatic Biological Assessment	3/14/24	
4	Wetland, Stream and Assessment Report	5/1/24	
5	MATA & BGEP Memo	3/14/24	
6	Hazmat Report	7/10/24	
7	NEPA/SEPA		9/1/24
8	Noise Exemption	3/25/24	
9	Hydraulic Project Approval		11/1/24

- Status of Agreements / Permits/ Easement
 City of Everett Public Work Permit In Progress
- Commitments with local Jurisdictions

No commitment with local Jurisdictions

❖ Top Risks

Budget

 Market conditions at bid opening may differ due to inflation and material availability

Design Schedule

Unanticipated utility relocation

Construction Schedule

Procurement of girders

Challenges

- Construction staging and traffic control for the improvements of the intersection of SR 526 and Everett Mall Way
 - Widening a bridge over the busy local street Casino Rd
