

# Leota Middle School Replacement Project Phase 1

Application to use GC | CM Delivery

Project Review Committee Meeting January 27, 2023

## **Agenda**

- 1. Introductions
- 2. Why GC|CM?
- 3. Project Scope
- 4. GC|CM Procurement Process
- 5. Schedule
- 6. Budget
- 7. Outreach
- 8. Q&A



#### **Introductions**



**Dri Ralph**Executive Director of Capital
Projects & Operations, NSD



**Todd Hall**Director of Capital Projects,
NSD



**Sung Joung**Planning & Design
Administrator, NSD




Ashley McClaran
GC/CM Advisor, OAC
Services



#### **Michael Tolley** Interim Superintendent As Needed (AN) **Project Team** Dri Ralph **Perkins Coie** Executive Director of Capital **Andrew Greene** Projects & Operations Legal Counsel Procurement 5% GC/CM Contract Advisor Design 5% As Needed Construction 5% **OAC Services** GC/CM Advisor **Ashley McClaran Todd Hall** Song Consulting, LLC Program Manager Director of Capital Projects **Young Sang Song** Procurement 20% Procurement 20% DBE/WMBE Advisor Design 10% Design 20% As Needed Construction 5% Construction 10% **Sung Joung Devlin Piplic** Planning and Design Construction Manager Administrator Procurement 20% Procurement 80% Design 20% Design 80% Construction 80% Construction 20% GC/CM Team **Design Team** Design Construction

School District

## Introductions – Northshore School District (NSD)

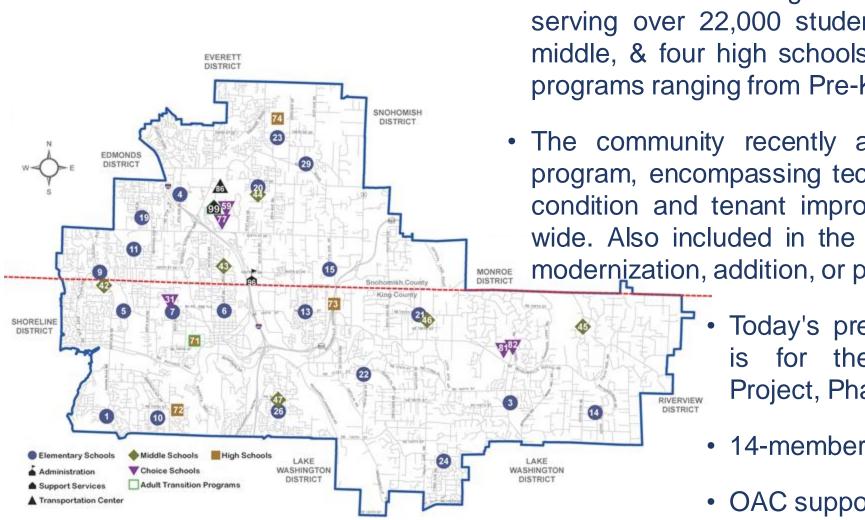

- NSD is one of the largest school districts in WA state, serving over 22,000 students at 20 elementary, six middle, & four high schools as well as seven choice programs ranging from Pre-K to beyond 12th grade.
- The community recently approved a \$425M bond program, encompassing technology, security, building condition and tenant improvement initiatives districtwide. Also included in the bond were 8 growth-type modernization, addition, or partial replacement sites.
  - Today's presentation and application is for the Leota Middle School Project, Phase I
  - 14-member capital project team
  - OAC support



## Why GC CM?

### **Complex Phasing and Site**

- Phased replacement
- Inflexible delivery schedule due to school calendar
- Ongoing operations during construction
- Ensure safety of students, staff and community






## Why GC CM?

#### **Opportunity for Greater Innovation and Efficiencies**

- Contractor input during design
- Early procurement
- Enhanced buying power
- Design for future flexibility

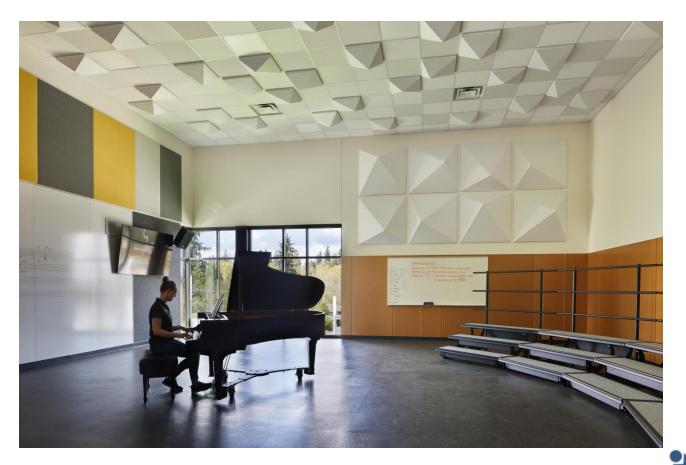


## Why GC CM?

#### **Public Benefit**

 Expedites project schedule through vetted existing conditions and phasing decisions

 Maintains educational operations during construction





## NSD 10-year Construction History > \$5million

Design Bid Build

**ESCO** 

GC CM

Kenmore Middle School Phase 3

Innovation Lab HS
Kokanee Elem
Lockwood Elem Ph1
East Ridge Elem

NSD Concert Hall
Skyview MS/Canyon
Creek Elem
Ruby Bridges Elem
Woodinville HS Ph2-3
North Creek HS

Budget: \$15.4m Final Cost: \$14.3m Combined Budget: \$34.7m Final Cost: \$32.7m Combined Budget: \$355.6m Final Cost: \$336.3



## **GC | CM Procurement Process**

NSD plans to use a three step GC|CM selection model:

- Request for Qualifications (RFQ)
  - · Focus on relevant experience, proposed team, and approach
- 2. Interviews
  - Interviews may include office visits
  - Focus on team members proposed for the work
- 3. Request for Fee Proposal (RFFP)
  - Fee and Specified General Conditions
  - Focus on competitive and reasonable fees



## **Project Scope**

#### **Leota Middle School**

- Increase classroom capacity
- Increase functional performance
- Improve supervision at entry and Admin
- Increase Commons and Gym Capacity
- Improve layout for better supervision






## **Project Scope**

#### **Leota Middle School**



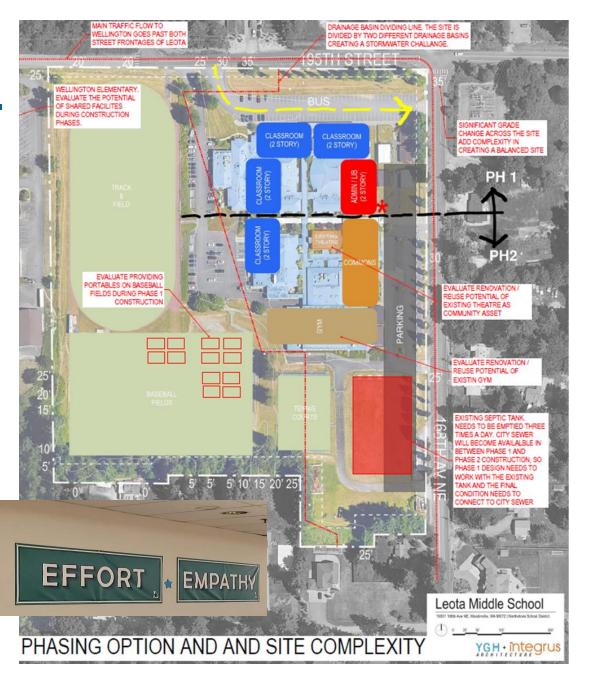



## **Schedule**

GC CM PROCUREMENT (Pending PRC Approval)		
Anticipated PRC Approval	January 27, 2023	
Issue RFQ	February 7, 2023	
SOQs Due	February 27, 2023	
Announce Shortlisted Finalists	March 10, 2023	
Interviews	March 17&20, 2023	
Issue RFFP to Finalists	March 22, 2023	
Public Fee Opening + Notice of Intent to Award	March 29, 2023	
GC CM Contracting	March 30, 2023 – May 2023	
DESIGN, CONSTRUCTION PHASE & OCCUPANCY		
Concept/Schematic Design	Jan 2023 – Sept 2023	
Design Development	Oct 2023 – Apr 2024	
Construction Documents (Permitting and Early Construction Packages)	May 2024 – Feb 2025	
· · · · · · · · · · · · · · · · · · ·	Nov 2024 – May 2026	
Construction	1101 2021 May 2020	
Substantial Completion	June 2026	



## **Budget and Funding**

PROJECT BUDGET	
Cost for Professional Services (A/E, Legal etc.)	\$3,6000,000
Estimated project construction costs (including construction contingencies)	\$45,000,000
Equipment and furnishing costs	\$1,350,000
Off-site costs	Included
Contract administration costs (owner, cm etc.)	\$1,350,000
Contingencies (design and owner)	\$2,250,000
Other related project costs (IT, permits, utilities, testing, inspection, moving)	\$1,950,000
Sales Tax	\$4,500,000
Total	\$60,000,000

**Funding** – The project is funded by a \$425M Bond passed by Northshore School District voters on February 8, 2022.



#### **Outreach**

- 10% Participation Goal
- Bond Program Outreach Meeting
- MWBE past performance evaluation & scoring
- MWBE & Small Business inclusion
- Song Consulting to assist the GC|CM Contractor
- Outreach & progress goals review
- Continued Engagement
- Reporting required for GC|CM projects







Leota Middle School Replacement Project

Phase 1
