



# Central Kitsap Solids and Liquids Hauled Waste Upgrades GCCM

PRC Hearing  
Alternative Selection Process for Mechanical Subcontractor

---

July 24, 2024

---

# Agenda

---


# Project Overview

- Kitsap County 2024-12
- GC/CM Services for Central Kitsap Treatment Plant(CKTP)
- WWTP built in stages in 1977; older and aging digesters - replacement and rehabilitation
- Design Flow 6 MGD
- Phased Construction
  - Group 1
    - » New Digester 3 & 4 with Control Building
    - » Thickening Building
    - » Septage Receiving Building
  - Group 2
    - » New Maintenance Building
    - » FOG Receiving Building
    - » Centrate Storage
    - » Pump Building
    - » Rehab Digester 1 & 2






# Central Kitsap Treatment Plant

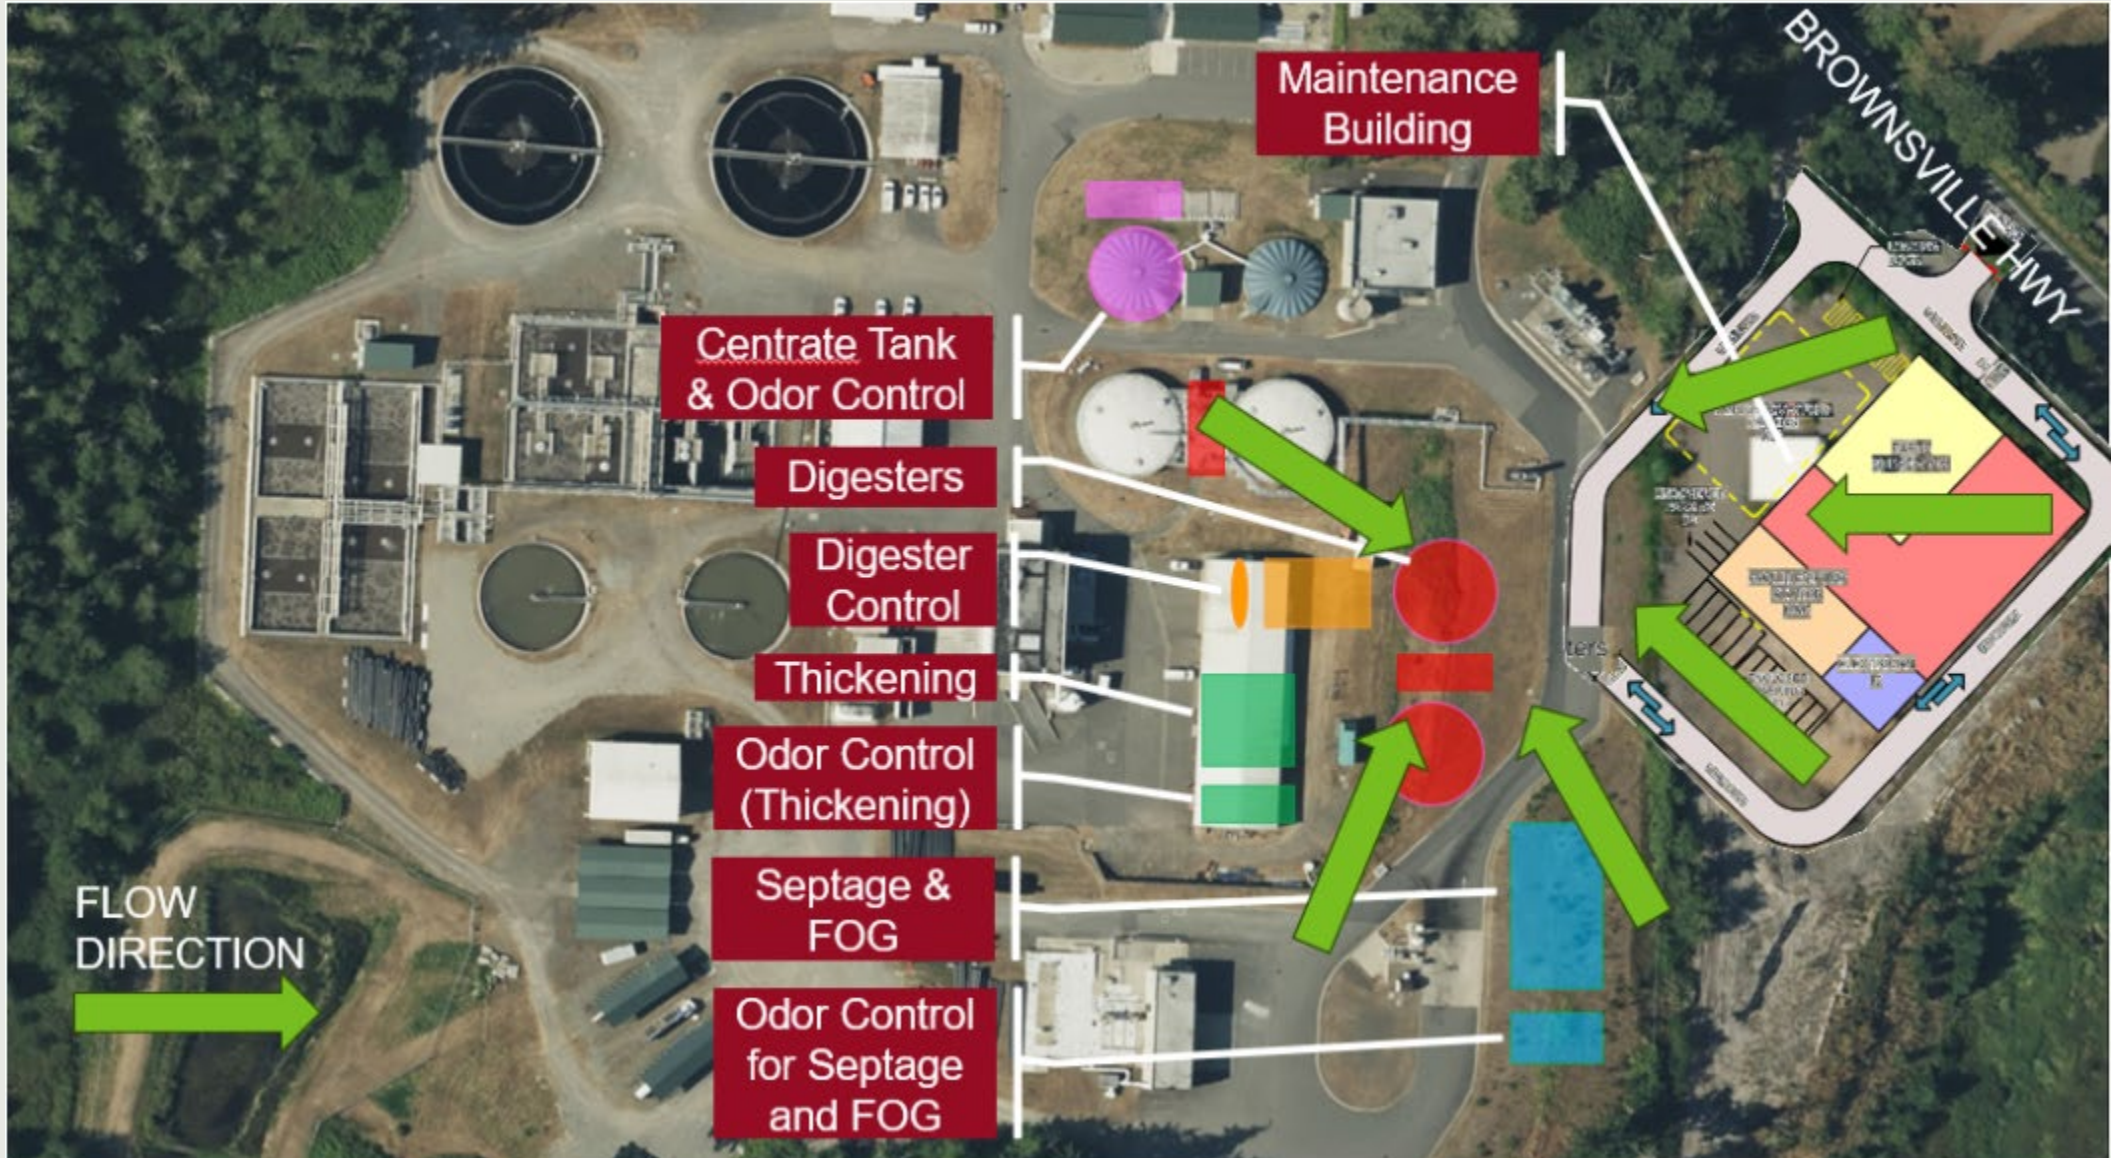




# MCCM Benefits

- Early Involvement in Development of Details and Process connections to existing systems
- Critical Path Work Certainty
  - Digester 3 and 4 input on equipment and coordination
- Review plant operations and constructability
  - Feedback on construction risk mitigation and implement strategies
  - Refined connection process and procedures in preconstruction
- Preconstruction Coordination in BIM and Equipment Shortlist
  - Schedule certainty on equipment lead times
  - Translates to efficient procurement after 90% Design issued.
  - Potential schedule savings of 3 months.
- Allow for Consistent SCADA/System integrator for Group 1 and 2
- Reliable Cost Estimating on Overall Project and ensuring accurate budget for Kitsap County
- Focused DEI planning and commitments in procurement process.

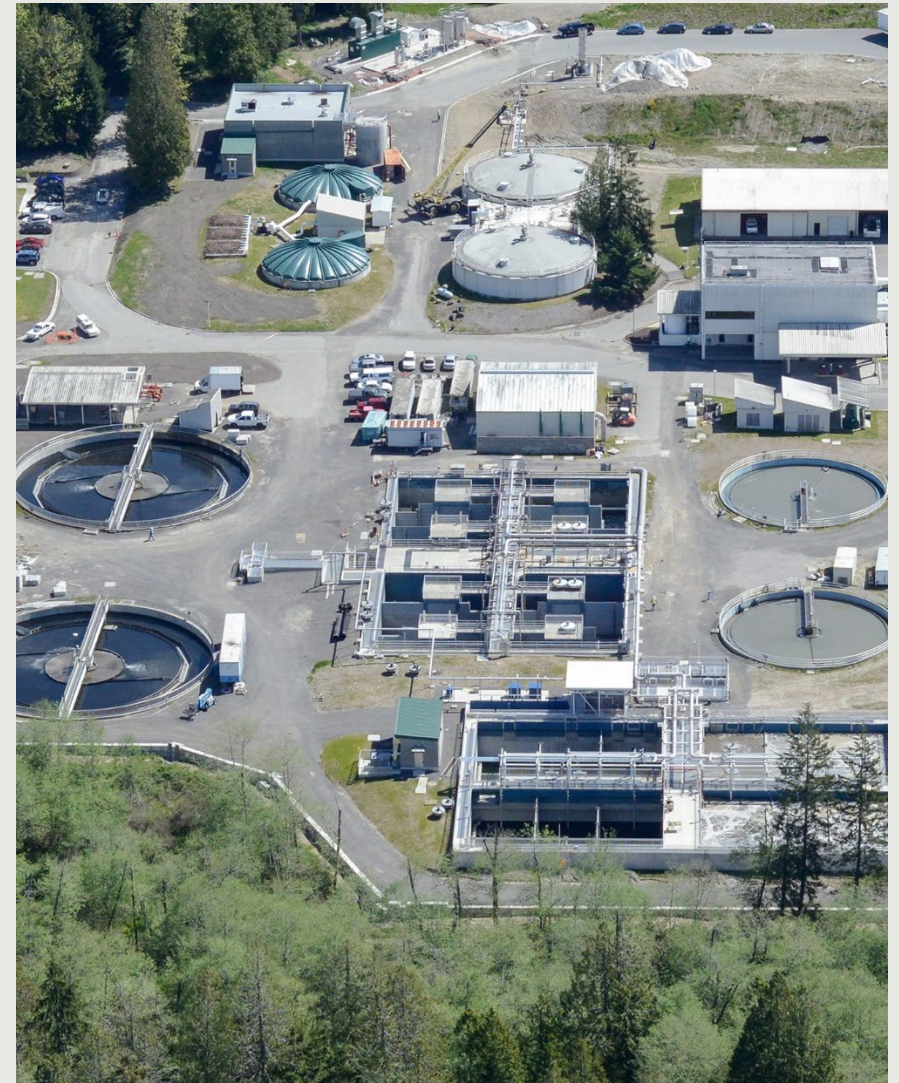

# Project Complexities

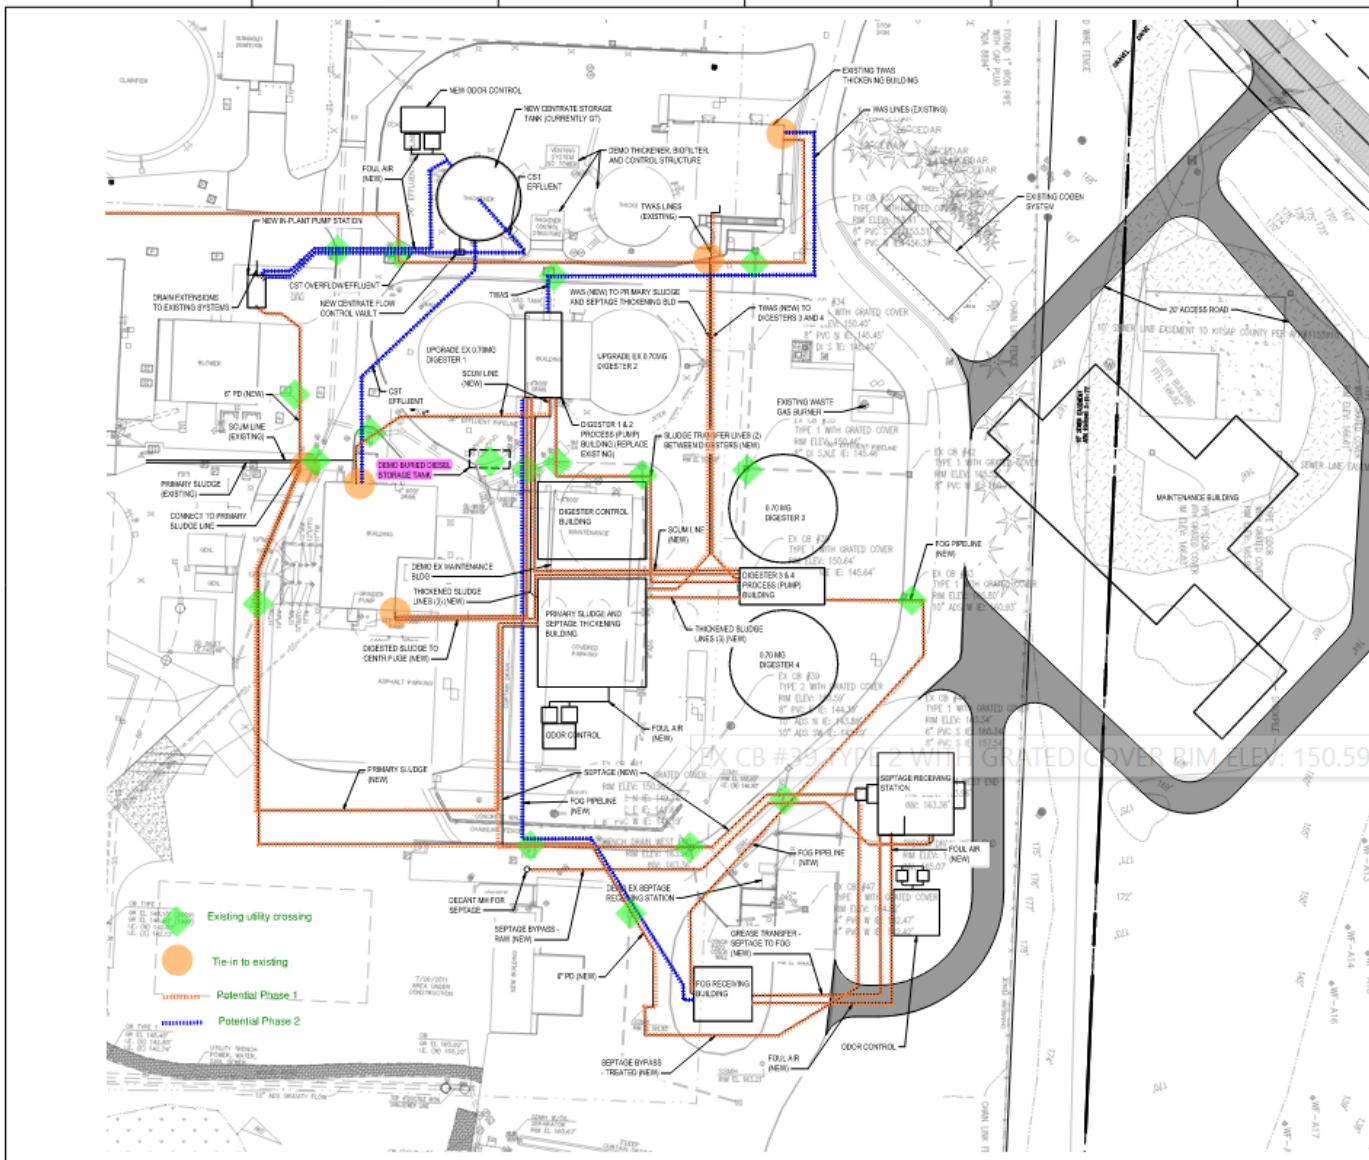

# Hoffman Construction MCCM Experience

Sound Transit

- U250 Station
- N140 Station
- N150 Station

Einstein Middle School

Kellogg Middle School

SeaTac Post IAF

State of Washington Newhouse Project

Coleman Dock Ferry Terminal



# Selection Process Schedule

Kitsap County Solids and Liquid Hauled Waste Upgrades

Activity #	ANTICIPATED MCCM PROCUREMENT SCHEDULE	Modified 6/20
01	Publish Notice of Intent for Alternate Selection Process	7/25/2024
02	Conduct Public Hearing	8/13/2024
03	Issue Written Determination	8/14/2024
04	Request for Qualifications (RFQ) Advertisement for Elec Services Issued	8/14/2024
05	Preproposal Informational Meeting (@1:00PM in person)	8/21/2024
06	Deadline for Questions on RFQ	8/23/2024
07	Issue Addendum to RFQ (if required)	8/27/2024
08	RFQ Response Submittal Deadline (@2:00PM)	9/3/2024
09	Selection Committee Review of RFQ's	9/9/2024
10	Notification of Most Qualified Firms	9/10/2024
11	Issue Request for Proposal (RFP, Fee/Bond/Insur only)	9/10/2024
12	Deadline for Questions on RFP	9/16/2024
13	Issue Addendum to RFP (if required)	9/17/2024
14	Interviews	9/17/2024
15	Submittal Deadline for RFP; Selection of Firm with highest total score	9/20/2024
16	Notification of Successful and Unsuccessful Firms and provide scoring summary	9/20/2024
17	Agreement for Preconstruction Services executed	9/27/2024





# Questions?

